



Cut & Bend Rebar – JOB ADVICE

















工作通知 Fax:6261 9133

BBS No 钢筋加工表	<u>MVR-TT-H315</u>	Total Weight 总重量	<u>1,013</u>
Contract 合同号码		Total Pages Attached 统计页数	1+7
Customer 承包商	<u>WOH HUP PTE LTD</u>	Gate:	
Project Title 施工地址	<u>MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906</u>		
Description 形容	L37层 CJ4-2 板 T2		
Date Order 订单日期	24-Aug-2026	Date Required 交货日期	31-Aug-2026
Remarks 评论			
Check/Approved By 检查/审核/订货人	<u>Zhou Bing</u>	Handphone 手提电话	<u>9847 1699</u>
Site Contact Person 联络人	<u>Kumar</u>	Handphone 手提电话	<u>8133 8587</u>
Material Receiver 收货人	<u>SIVA</u>	Handphone 手提电话	<u>8426 2921</u>
Site Telephone 工地电话		Site Fax No 传真号码	
Scheduler 开料人	<u>Lu Yong Bing</u>	Handphone 手提电话	<u>8982 7022</u>
<u>***Please Allow 5 days for ??? To Process Your Order***</u>			
<u>51 Tuas South Street 5,Singapoer637644</u>			

Name	Contact numbers	Email Address
project Coodinator	Leslie LIM	8524 2927



PROJECT :	MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906		Pg. 1 / 7
BBS No:	MVR-TT-H315	Rev.	Date : 2026/8/24
Dwg. No.		Rev.	Prepared By:
TITLE:	L37层 CJ4-2 板 T2		BBS NO: MVR-TT-H315














BAR BENDING SCHEDULE									
MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO.O F EACH	TOTAL	SHAP E CODE	SHAPE	CUT OFF LENGTH	WEIGHT
					T2				
	50	H 10	1	8	8	54		1500	7.39
	51	H 10	1	5	5	37		1850	5.70
	52	H 10	1	4	4	54		3000	7.39
	53	H 10	1	10	10	37		3850	23.72
	54	H 10	1	4	4	37		3750	9.24
	55	H 10	1	2	2	37		4300	5.30
	56	H 10	1	6	6	37		3130	11.57
	57	H 10	1	12	12	37		2600	19.22
	58	H 10	1	8	8	37		3130	15.42
	59	H 10	1	2	2	54		2280	2.81
	60	H 10	1	5	5	54		1230	3.79
	61	H 10	1	3	3	38a		580	1.07
	62	H 10	1	1	1	38a		310	0.19
	63	H 10	1	1	1	54		1090	0.67
	64	H 10	1	3	3	54		570	1.05
	65	H 10	1	2	2	54		1910	2.35
	66	H 10	1	5	5	38a		3070	9.46

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				####							126.3 KG



PROJECT :		MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906	Pg. 2 / 7
BBS No:		MVR-TT-H315	Rev. Date : 2026/8/24
Dwg. No.			Rev. Prepared By:
TITLE:		L37层 CJ4-2 板 T2	BBS NO: MVR-TT-H315

BAR BENDING SCHEDULE

MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO. OF EACH	TOTAL	SHAPE CODE	SHAPE	CUT OFF LENGTH	WEIGHT
	67	H 10	1	1	1	54		2580	1.59
	68	H 10	1	14	14	54		2700	23.28
	69	H 10	1	14	14	54		3490	30.10
	70	H 10	1	1	1	38a		4180	2.57
	71	H 10	1	1	1			4080	2.51
	72	H 10	1	9	9	37		6350	35.20
	73	H 10	1	9	9	54		4690	26.00
	74	H 10	1	4	4			8020	19.76
	75	H 10	1	4	4			8020	19.76
	76	H 10	1	9	9	54		4690	26.00
	77	H 10	1	9	9	37		6350	35.20
	78	H 10	1	1	1			4080	2.51
	79	H 10	1	1	1			2920	1.80
	80	H 10	1	5	5	54		2720	8.38
	81	H 10	1	2	2			1930	2.38
	82	H 10	1	1	1	37		700	0.43
	83	H 10	1	1	1	38a		360	0.22
	84	H 10	1	3	3	38a		630	1.16

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				####							238.9 KG



PROJECT :	MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906	Pg. 3 / 7
BBS No:	MVR-TT-H315	Rev. Date : 2026/8/24
Dwg. No.		Rev. Prepared By:
TITLE:	L37层 CJ4-2 板 T2	BBS NO: MVR-TT-H315

BAR BENDING SCHEDULE

MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO. OF EACH	TOTAL	SHAPE CODE	SHAPE	CUT OFF LENGTH	WEIGHT
	85	H 10	1	5	5			1260	3.88
	86	H 10	1	2	2			2360	2.91
	87	H 10	1	1	1			4870	3.00
	88	H 10	1	14	14	54		2700	23.28
	89	H 10	1	14	14	54		3490	30.10
	90	H 10	1	14	14	54		3210	27.68
	91	H 10	1	15	15	54		2700	24.95
	92	H 10	1	2	2			2360	2.91
	93	H 10	1	5	5			1260	3.88
	94	H 10	1	3	3	38a		630	1.16
	95	H 10	1	1	1	38a		360	0.22
	96	H 10	1	1	1	37		700	0.43
	97	H 10	1	2	2			1930	2.38
	98	H 10	1	6	6	54		2720	10.05
	99	H 10	1	2	2	38a		300	0.37
	100	H 10	1	2	2	37		1160	1.43
	101	H 10	1	2	2	37		900	1.11
	102	H 10	1	1	1			1080	0.67

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				####							140.4 KG



PROJECT :	MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906	Pg. 4 / 7
BBS No:	MVR-TT-H315	Rev. Date : 2026/8/24
Dwg. No.		Rev. Prepared By:
TITLE:	L37层 CJ4-2 板 T2	BBS NO: MVR-TT-H315

BAR BENDING SCHEDULE

MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO. OF EACH	TOTAL	SHAPE CODE	SHAPE	CUT OFF LENGTH	WEIGHT
	103	H 10	1	3	3			980	1.81
	104	H 10	1	3	3			1540	2.85
	105	H 10	1	2	2	54		2620	3.23
	106	H 10	1	3	3			1730	3.20
	107	H 10	1	1	1			1640	1.01
	108	H 10	1	11	11	54		2800	18.97
	109	H 10	1	12	12	54		4440	32.82
	110	H 10	1	1	1			5500	3.39
	111	H 10	1	14	14	54		7560	65.20
	112	H 10	1	5	5	37		1050	3.23
	113	H 10	1	2	2	37		3150	3.88
	114	H 10	1	2	2	38a		6120	7.54
	115	H 10	1	5	5	54		7130	21.96
	116	H 10	1	2	2	38a		5990	7.38
	117	H 10	1	5	5	54		4330	13.34
	118	H 10	1	5	5	37		1050	3.23
	119	H 10	1	2	2	37		3150	3.88
	120	H 10	1	4	4	38a		3230	7.96

REBAR SIZE		R06	H8	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				####							204.9 KG



PROJECT :			MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906						Pg. 5 / 7			
BBS No:			MVR-TT-H315					Rev.		Date : 2026/8/24		
Dwg. No.								Rev.		Prepared By:		
TITLE:			L37层 CJ4-2 板 T2						BBS NO:		MVR-TT-H315	
BAR BENDING SCHEDULE												
MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO.O F EACH	TOTAL	SHAP E CODE	SHAPE			CUT OFF LENGTH	WEIGHT	
	121	H 10	1	1	1	38	70	2620	200	2890	1.78	
	122	H 10	1	7	7	37	100	950		1050	4.53	
	123	H 10	1	1	1		100	130 1190	100	1520	0.94	
	124	H 10	1	2	2	37	100	1400		1500	1.85	
	125	H 10	1	3	3	38	100	2860	160	3120	5.77	
	126	H 10	1	6	6		100	130 5130	100	5460	20.18	
	127	H 10	1	2	2	38	100	2860	160	3120	3.84	
	53a	H 10	1	1	1	37	100	550		650	0.40	
				T2ADD								
	9	H 10	1	6	6	37	190	2000		2190	8.09	
	10	H 10	1	5	5	20	2240			2240	6.90	
	11	H 13	1	11	11	20	2000			2000	22.92	
	12	H 13	1	12	12	20	2000			2000	25.01	
				洞加T								
	17	H 16	1	2	2	37	780	1280		2060	6.51	

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				54.3	47.9	6.5					108.7 KG



PROJECT :	MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906	Pg. 6 / 7
BBS No:	MVR-TT-H315	Rev. Date : 2026/8/24
Dwg. No.		Rev. Prepared By:
TITLE:	L37层 CJ4-2 板 T2	BBS NO: MVR-TT-H315











BAR BENDING SCHEDULE

MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO. OF EACH	TOTAL	SHAPE CODE	SHAPE	CUT OFF LENGTH	WEIGHT
	18	H 16	1	2	2	37	250 1650	1900	6.00
	19	H 16	1	1	1	38	500 350 600	1450	2.29
	20	H 16	1	1	1	20	2580	2580	4.07
	21	H 16	1	2	2	20	2580	2580	8.15
	22	H 16	1	1	1	37	1100 1300	2400	3.79
	23	H 16	1	2	2	54	250 1300 530	2080	6.57
	24	H 16	1	2	2	20	2400	2400	7.58
	25	H 16	1	2	2	20	3200	3200	10.11
	25a	H 16	2	2	4	20	2700	2700	17.05
	26	H 16	2	2	4	20	2180	2180	13.77
	27	H 16	2	1	2	37	1100 1300	2400	7.58
	28	H 16	1	1	1	38a	600 2390 600	3590	5.67
	28a	H 16	1	1	1	38a	530 2350 530	3410	5.38
	29	H 16	1	1	1	20	4960	4960	7.83
	30	H 16	1	2	2	20	4960	4960	15.66
	31	H 16	2	1	2	37	650 1670	2320	7.33
	32	H 16	1	2	2	20	2180	2180	6.88




REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT						####					135.8 KG



PROJECT :	MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906		Pg. 7 / 7
BBS No:	MVR-TT-H315	Rev.	Date : 2026/8/24
Dwg. No.		Rev.	Prepared By:
TITLE:	L37层 CJ4-2 板 T2		BBS NO: MVR-TT-H315



BAR BENDING SCHEDULE									
MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO.O F EACH	TOTAL	SHAP E CODE	SHAPE	CUT OFF LENGTH	WEIGHT
	33	H 16	1	2	2	20		2340	7.39
	34	H 16	1	2	2	37		2130	6.73
	35	H 16	1	1	1	38		1450	2.29
	36	H 16	1	1	1	20		2340	3.69
	37	H 16	1	2	2	20		3180	10.04
	38	H 16	1	1	1	38		3280	5.18
	39	H 16	1	2	2	20		2340	7.39
	40	H 16	1	1	1	38		1950	3.08
	41	H 16	1	2	2	20		2340	7.39
	42	H 16	1	2	2	20		1610	5.08




REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT						58.3					58.3 KG

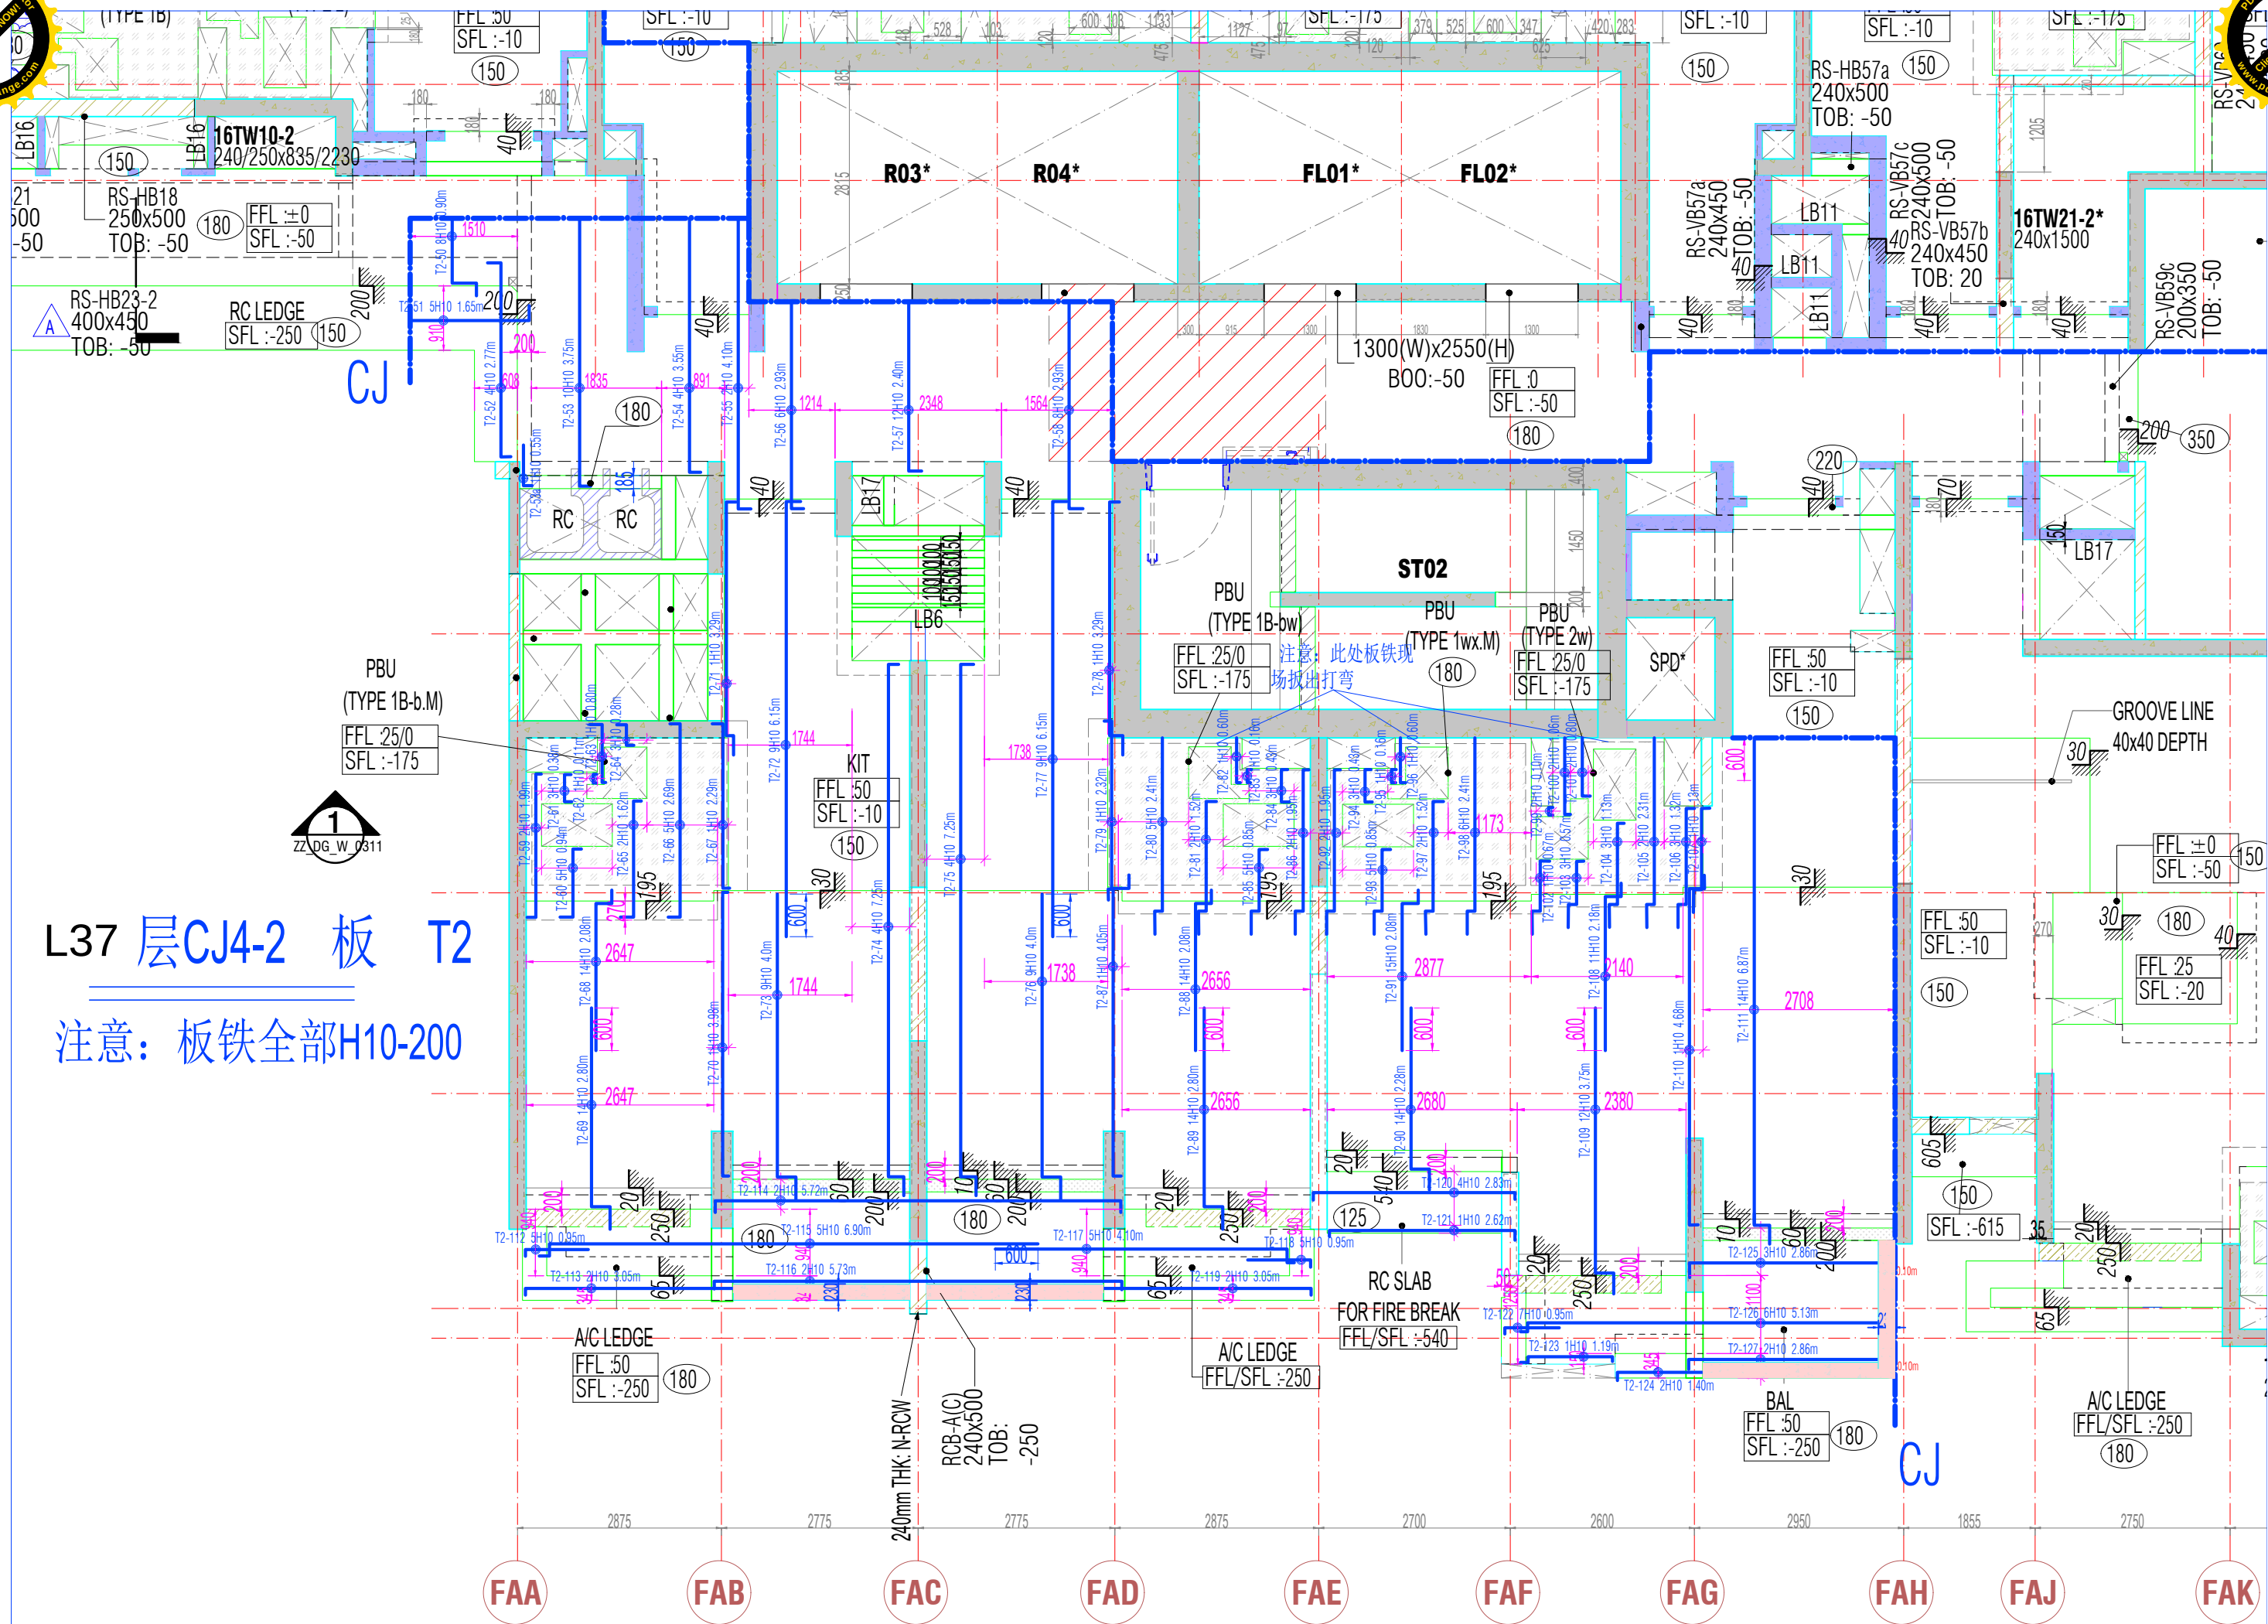

L37 层CJ4-2 板 T2

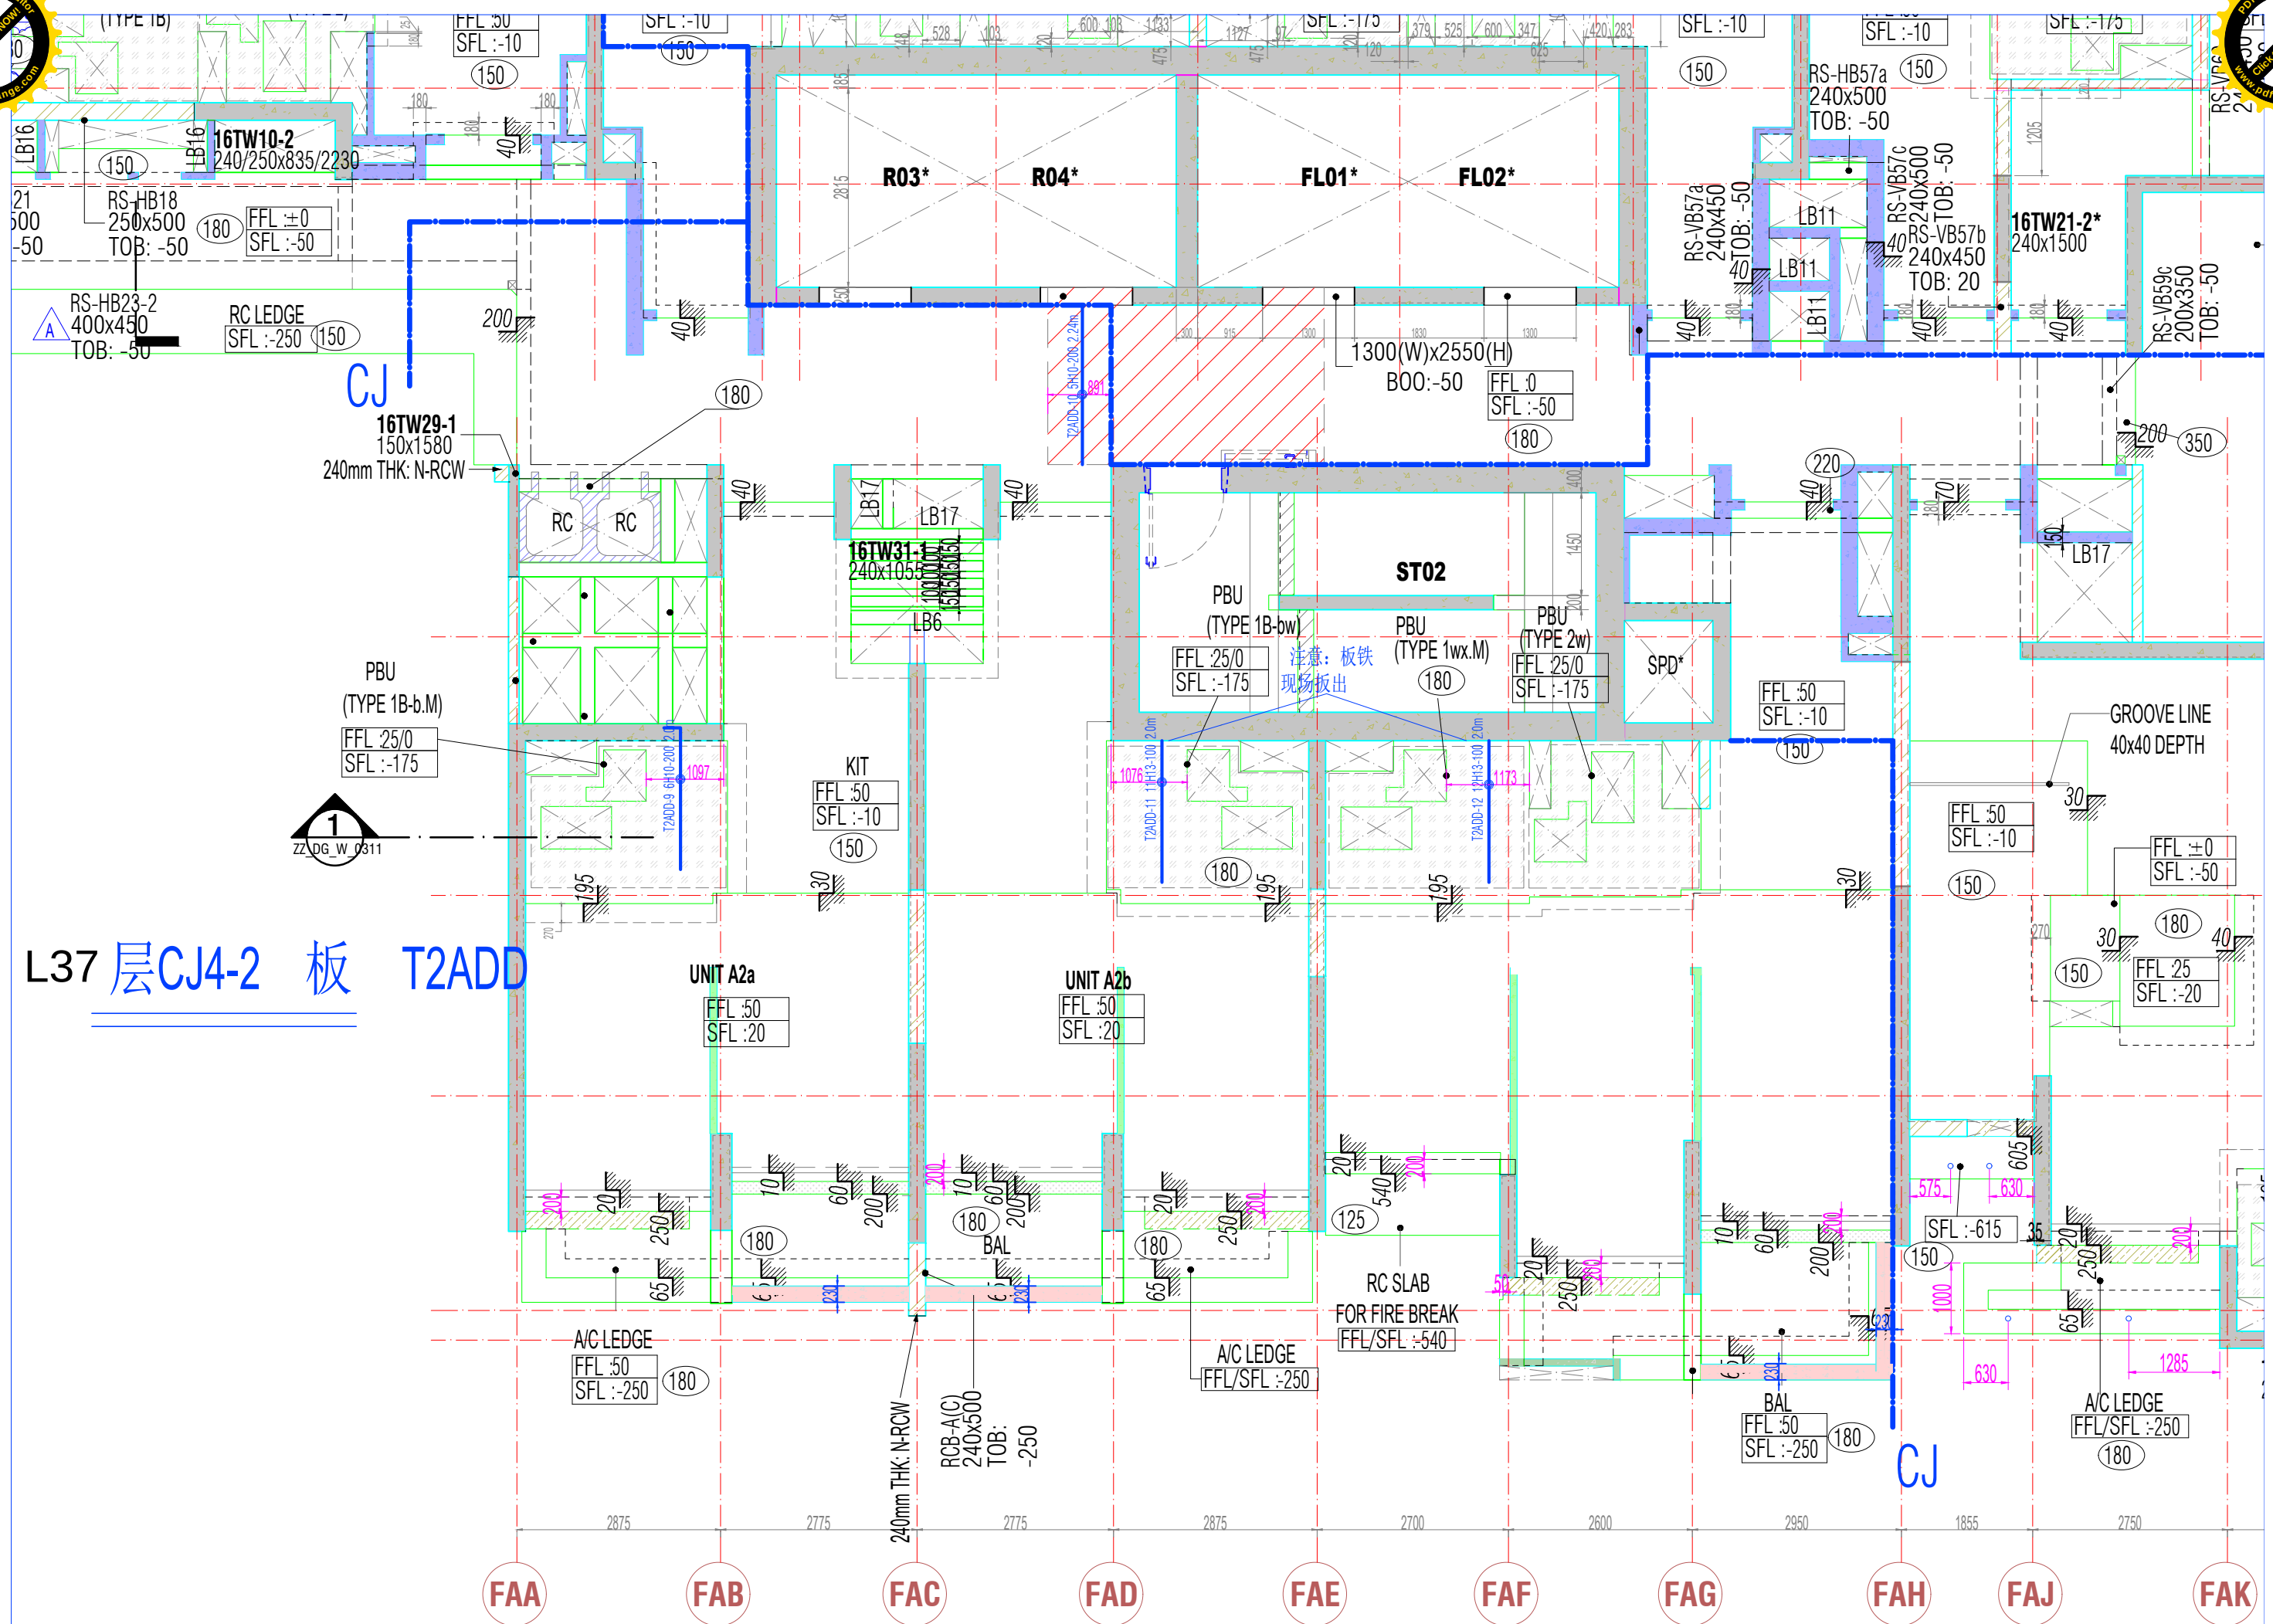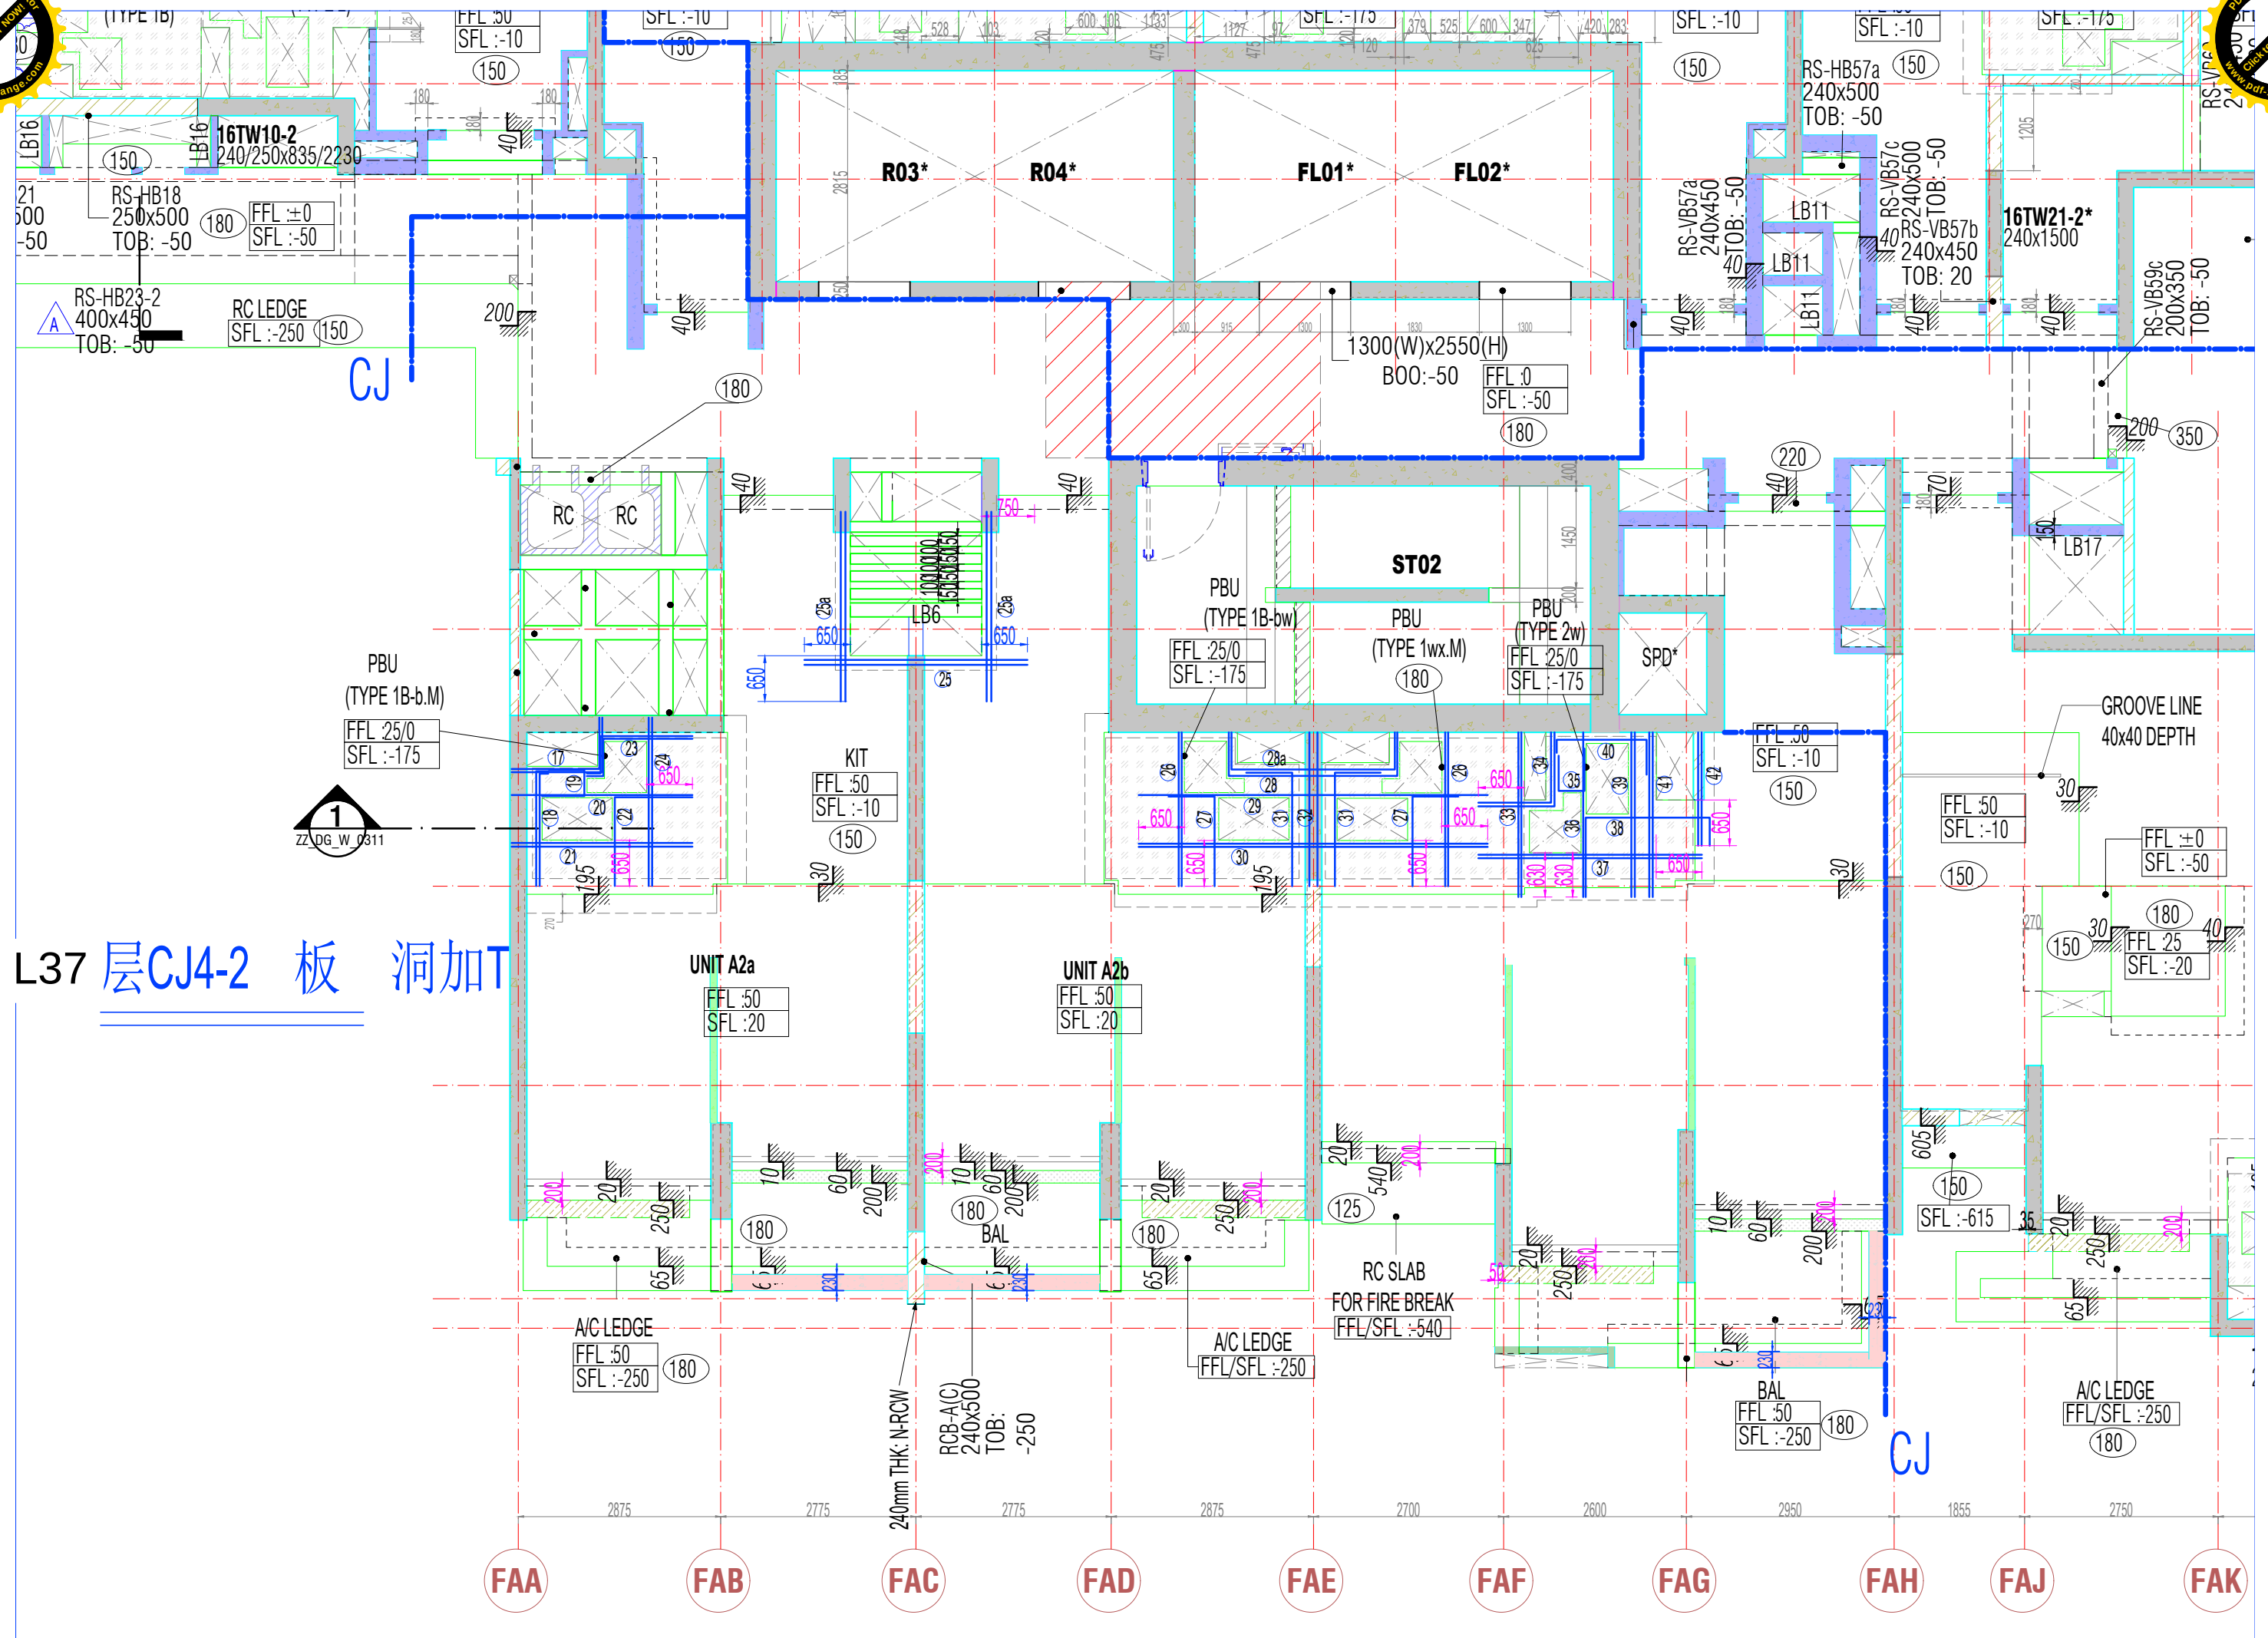注意：板铁全部H10-200





L37 层CJ4-2 板洞加T



洞加T:

- ①7 2H16 1.28/0.78m
- ①8 2H16 1.65/0.25m
- ①9 1H16 0.60/0.35/0.50m
- ②0 1H16 2.58m
- ②1 2H16 2.58m
- ②2 1H16 1.10/1.30m
- ②3 2H16 1.30/0.53/0.25m
- ②4 2H16 2.40m

- ②5 2H16 3.20m
- ②5a 2*2H16 2.70m

- ②6 2*2H16 2.18m
- ②7 2*1H16 1.30/1.10m
- ②8 1H16 0.60/2.39/0.60m
- ②8a 1H16 0.53/2.35/0.53m
- ②9 1H16 4.96m
- ③0 2H16 4.96m
- ③1 2*1H16 1.67/0.65m
- ③2 2H16 2.18m

- ③3 2H16 2.34m
- ③4 2H16 1.03/1.10m
- ③5 1H16 0.60/0.35/0.50m
- ③6 1H16 2.34m
- ③7 2H16 3.18m
- ③8 1H16 1.13/1.75/0.40m
- ③9 2H16 2.34m
- ④0 1H16 0.25/1.30/0.40m
- ④1 2H16 2.34m
- ④2 2H16 1.61m



MVR PJW CO WH CST ZZ ZZ SK W 2546F
Revised Beam & Slab Schedule for L17 and above (Amendment to ST19)

- NOTES:
UNLESS NOTED OTHERWISE,
1. SLAB REINFORCEMENTS SHALL BE H10-200 (B/W).
2. SLAB THICKNESS SHALL BE 180.
3. REINFORCEMENT LAPPING LENGTH TO BE TL.
4. FOR REINF. THAT EXCEEDS 12m, THE LAPPING SHOULD BE DONE WHERE STRESS IS LESS. THE LAPPING OF TOP REINFORCEMENT SHOULD BE AWAY FROM SUPPORTS WHERE STRESS IS HIGH.
5. — DENOTES ADDITIONAL REINFORCEMENT.
6. TRIMMER BARS FOR OPENINGS, REFER TO DWG. NO. 21.070/N2 FOR DETAILS.

23 sheet of 25

PC 13/17

BUILDING AND CONSTRUCTION ACT
APPROVED UNDER SECTION 5 / SECTION 5
BUILDING CONTROL ACT (CHAPTER 29)

Project Ref No : A1252-00566-2022-ST19

for Commissioner of Building Control

PE'S CERTIFICATION



AC'S CERTIFICATION

ACCREDITED CHECKER

NO:1089

KOK KING MIN
In AC Organisation
Registration No: A054
BUILDING CONTROL ACT
SINGAPORE

CONSTRUCTION SKETCH

ISSUED

17 NOV 2025

KTP CONSULTANTS PTE LTD

REV	AMENDMENTS	DR	DES	CHK	DATE
4	REVISED SLAB REINFORCEMENT				11.17.25
3	REVISED SLAB REINFORCEMENT				26.09.25
2	REVISED SLAB REINFORCEMENT				17.09.25
1	REVISED SLAB REINFORCEMENT				05.03.25

PROJECT

PROPOSED NEW ERECTION OF 51 STOREY MIXED USE DEVELOPMENT COMPRISING 5 STOREY HOTEL AND CARPARK PODIUM, 9 STOREY HOTEL (350 ROOMS), 36/37 STOREY RESIDENTIAL FLATS (683 UNITS) AND 2 BASEMENTS ON LOTS 00483K AND 00484N TS 30 AND SUBTERRANEAN SPACE LOT 800772C TS 30 AT MARINA VIEW (DOWNTOWN CORE PLANNING AREA)

ARCHITECT

ARCHITECT 61 PTE. LTD.

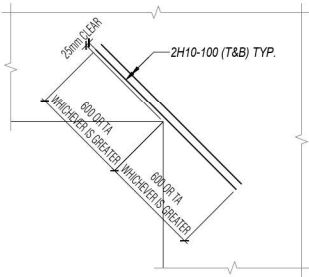
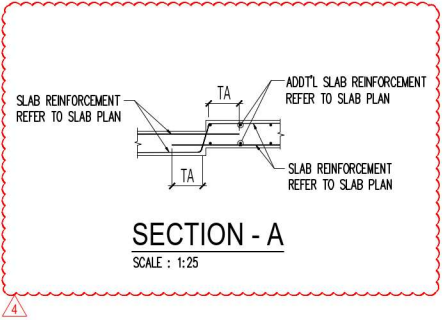
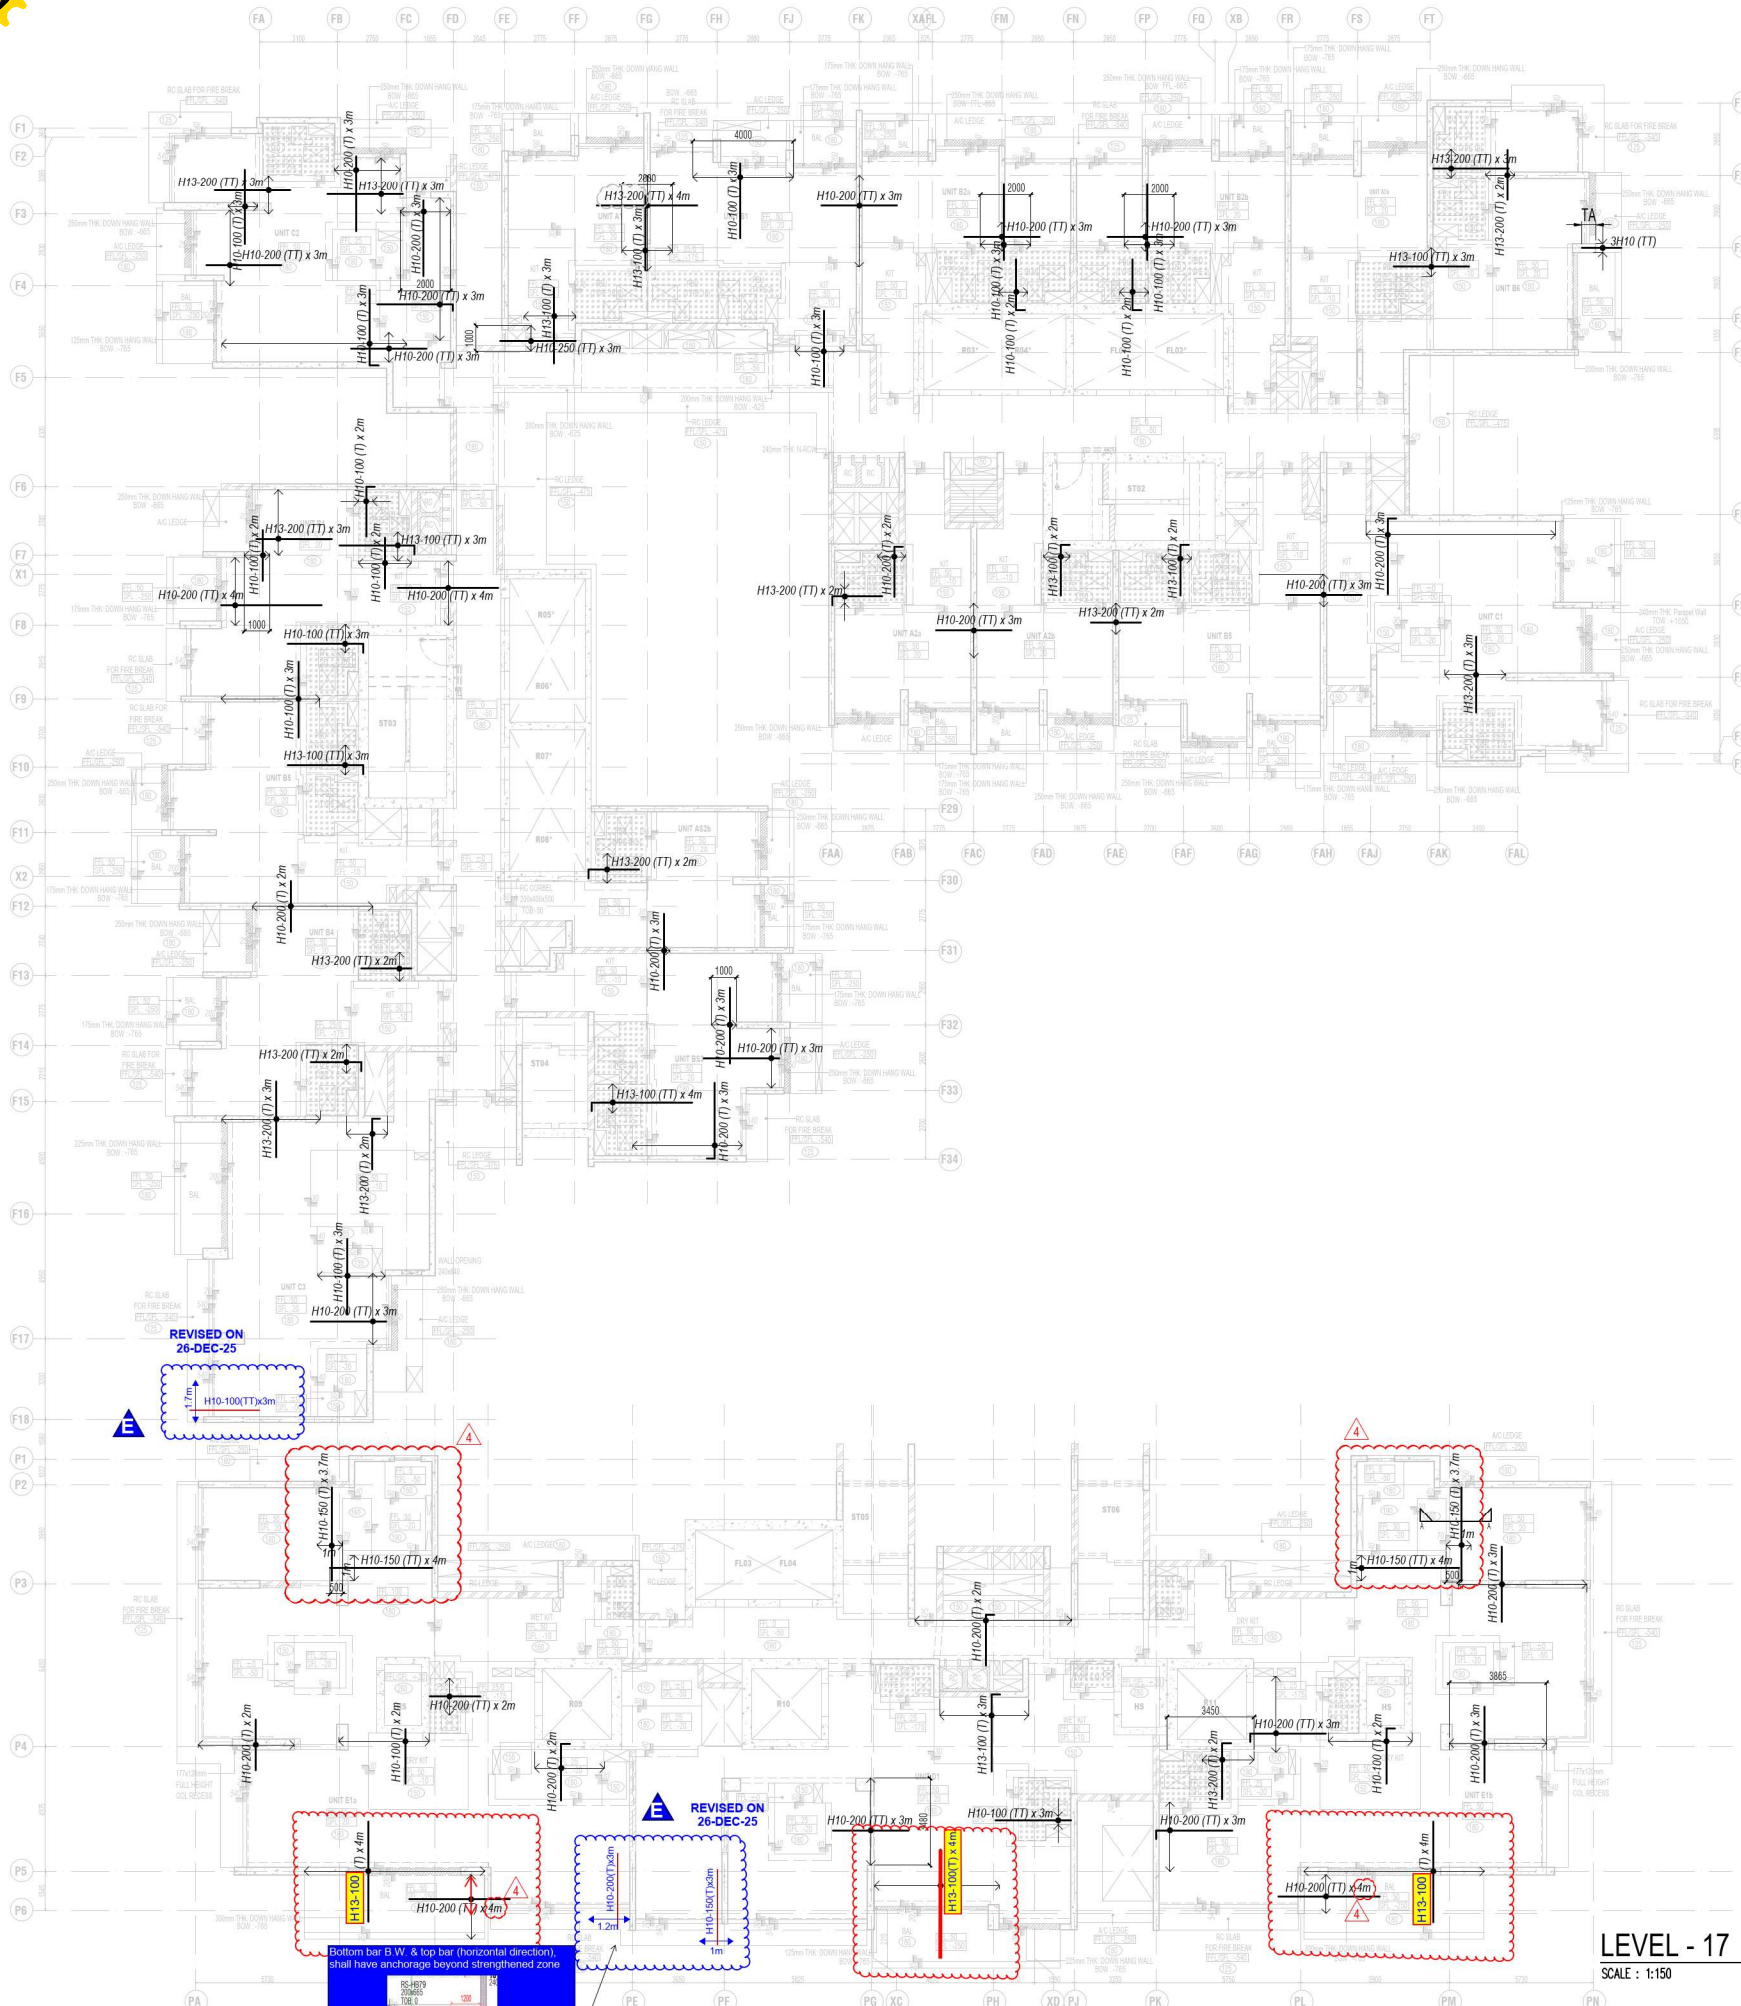
KTP **KTP Consultants Pte Ltd**
Surbana Jurong Campus 38 Cleantech
Loop, #01-31 Singapore 636741
Tel : +65 6248 1288

DRAWN: CH DATE: DESIGNED: JS/AP/PS
SCALE: AS SHOWN CHECKED: ChewAL

DWG. NO. 21.070/L17S1

LEVEL - 17 TO L33, L36 TO L48 TYPICAL SLAB TOP REINFORCEMENT LAYOUT

THE OWNERSHIP OF THE COPYRIGHT IN THIS DRAWING IS RETAINED BY KTP CONSULTANTS. WHOSE CONSENT MUST BE SOUGHT BEFORE ANY USE OR REPRODUCTION OF THE DRAWING OR ANY PART THEREOF CAN BE MADE.



TYPICAL TRIMMER BARS AT RE-ENTRANT CORNER
SCALE: 1:25

LEVEL - 17 TO L33, L36 TO L48 TYPICAL SLAB TOP REINFORCEMENT LAYOUT
SCALE: 1:150
