











Cut & Bend Rebar – JOB ADVICE

工作通知 Fax:6261 9133

BBS No 钢筋加工表	<u>MVR-TT-H317</u>	Total Weight 总重量	<u>333</u>
Contract 合同号码		Total Pages Attached 统计页数	1+2
Customer 承包商	<u>WOH HUP PTE LTD</u>	Gate:	
Project Title 施工地址	<u>MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906</u>		
Description 形容	L37层CJ4-2 板上插铁		
Date Order 订单日期	24-Aug-2026	Date Required 交货日期	31-Aug-2026
Remarks 评论			
Check/Approved By 检查/审核/订货人	<u>Zhou Bing</u>	Handphone 手提电话	<u>9847 1699</u>
Site Contact Person 联络人	<u>Kumar</u>	Handphone 手提电话	<u>8133 8587</u>
Material Receiver 收货人	<u>SIVA</u>	Handphone 手提电话	<u>8426 2921</u>
Site Telephone 工地电话		Site Fax No 传真号码	
Scheduler 开料人	<u>Lu Yong Bing</u>	Handphone 手提电话	<u>8982 7022</u>
<u>***Please Allow 5 days for ??? To Process Your Order***</u>			
<u>51 Tuas South Street 5,Singapoer637644</u>			

Name	Contact numbers	Email Address
project Coodinator	Leslie LIM	8524 2927



PROJECT :		MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906						Pg. 1 / 2	
BBS No:		MVR-TT-H317						Rev.	Date : 2026/8/24
Dwg. No.								Rev.	Prepared By:
TITLE:		L37层CJ4-2 板上插铁						BBS NO: MVR-TT-H317	
BAR BENDING SCHEDULE									
MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO.O F EACH	TOTAL	SHAP E CODE	SHAPE	CUT OFF LENGTH	WEIGHT
				小坎					
	1# 宽度不等 +350mm高								
立-300	板位	H 10	1	152	152		250 	840	78.65
水平-300	现场剪配	H 10	1	20	20	20		4000	49.28
	2# 100mm宽 +200mm高								
立-300		H 10	1	40	40		250 	700	17.25
水平-300	现场剪配	H 10	1	8	8	20		4000	19.71
	3# 230mm宽 -25mm高								
外立-300		H 10	1	35	35		250 	760	16.39
内立-300		H 10	1	34	34		250 	760	15.92
水平-300	现场剪配	H 10	2	6	12	20		4000	29.57
	4#素灰加铁 175mm宽 200mm高								
立-200		H 10	1	40	40	37	370 	690	17.00
引铁		H 13	2	1	2	20		3000	6.25
		H 13	1	1	1	20		2900	3.02

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				####	9.3						253 KG



PROJECT :		MARINA VIEWLP 28F 1 STRAITS BIVD,SINGAPORE 018906	Pg. 2 / 2
BBS No:		MVR-TT-H317	Rev. Date : 2026/8/24
Dwg. No.			Rev. Prepared By:
TITLE:		L37层CJ4-2 板上插铁	BBS NO: MVR-TT-H317

BAR BENDING SCHEDULE									
MEMBER	BAR MARK	TYPE & SIZE	NO. OF MBRS	NO. OF EACH	TOTAL	SHAPE CODE	SHAPE	CUT OFF LENGTH	WEIGHT
		5# 100mm宽 -170mm高							
立-300		H 10	1	8	8	37	240 240	480	2.37
水平-300		H 10	1	2	2	20	3000	3000	3.70
		6# 225mm宽 -100mm高							
立-300		H 10	3	4	12	54	170 170 240	580	4.29
水平-300		H 10	3	4	12	20	320	320	2.37
				7# 凹角加铁					
T/B		H 10	2	2	4	20	1200	1200	2.96
			8# 板平电线管加拉勾						
。 300/300		H 10	1	200	200		100 120 90 70	380	46.82
		H 10	1	80	80		100 90 90 70	350	17.25

REBAR SIZE		R06	H08	H10	H13	H16	H20	H25	H32	H40	TOTAL
WEIGHT				79.7							79.7 KG


KERB SCHEDULE:

1 #




RC KERB (WIDTH VARIES) TOK: + 350

2 #



RC KERB (WIDTH VARIES) TOK: + 200

3 #



RC KERB (WIDTH VARIES) TOK: -25

5 #



RC KERB (WIDTH VARIES) TOK: -170

6 #



RC KERB (WIDTH VARIES) TOK: -100



MVR PJW CO WH CST ZZ ZZ SK W 2427 A

Typical RC Kerb Detail Rev A

RC Kerb supporting Architectural Wall

Previously approved

H10-300 (See Kerb Details A-D)

H10 (See Kerb Details A-D)


Add'l H10

Kerb Elevation with Facade Recess

300x400x50D Facade Recess

KTP: WH to take note the kerb details are to support archi wall upto 3.5m. If the kerb detail is to be used for a higher architectural wall, it shall be subject to KTP's approval.

KERKYX 20250723

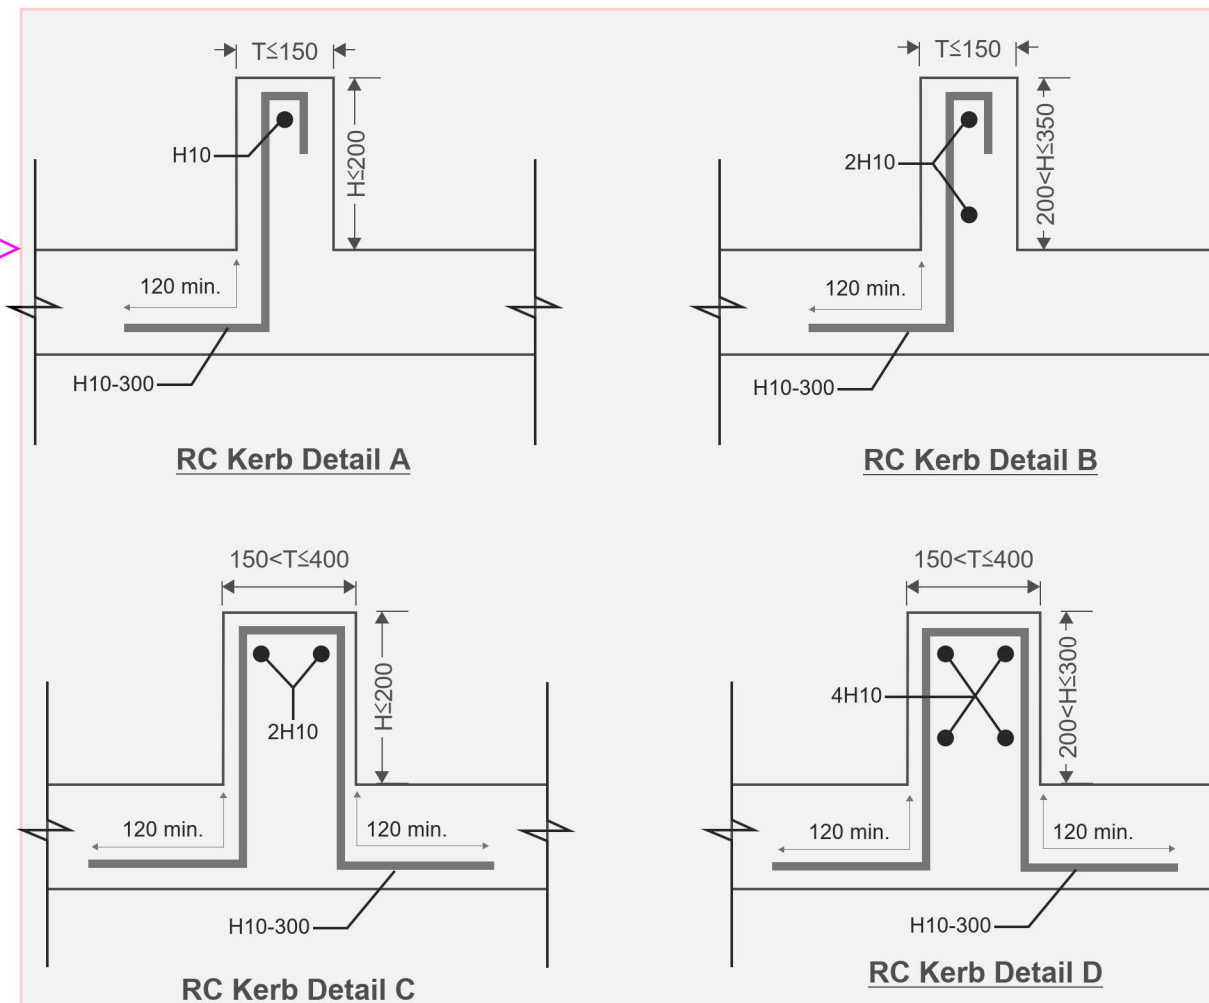



Copy to
1. PD - Chen Han Qi
2. PM - Wong Wei Siong
3. SE
4. RE/RTO
5. All Subcons
6. MVR WH, MVR Site
7. WH QS
8. WH Rebar Scheduler
9. DC
10. IOI - Muliadi, How See, Darren

From: Joseph Chin
20-May-25


KTP: No objection
20250520

CIVIL & STRUCTURAL ENGINEER KTP Consultants Pte Ltd			
APPROVED			
APPROVED (AP)	APPROVED WITH COMMENTS (AC)	REVISE AND RESUBMIT (RR)	REJECTED (R)
	✓		

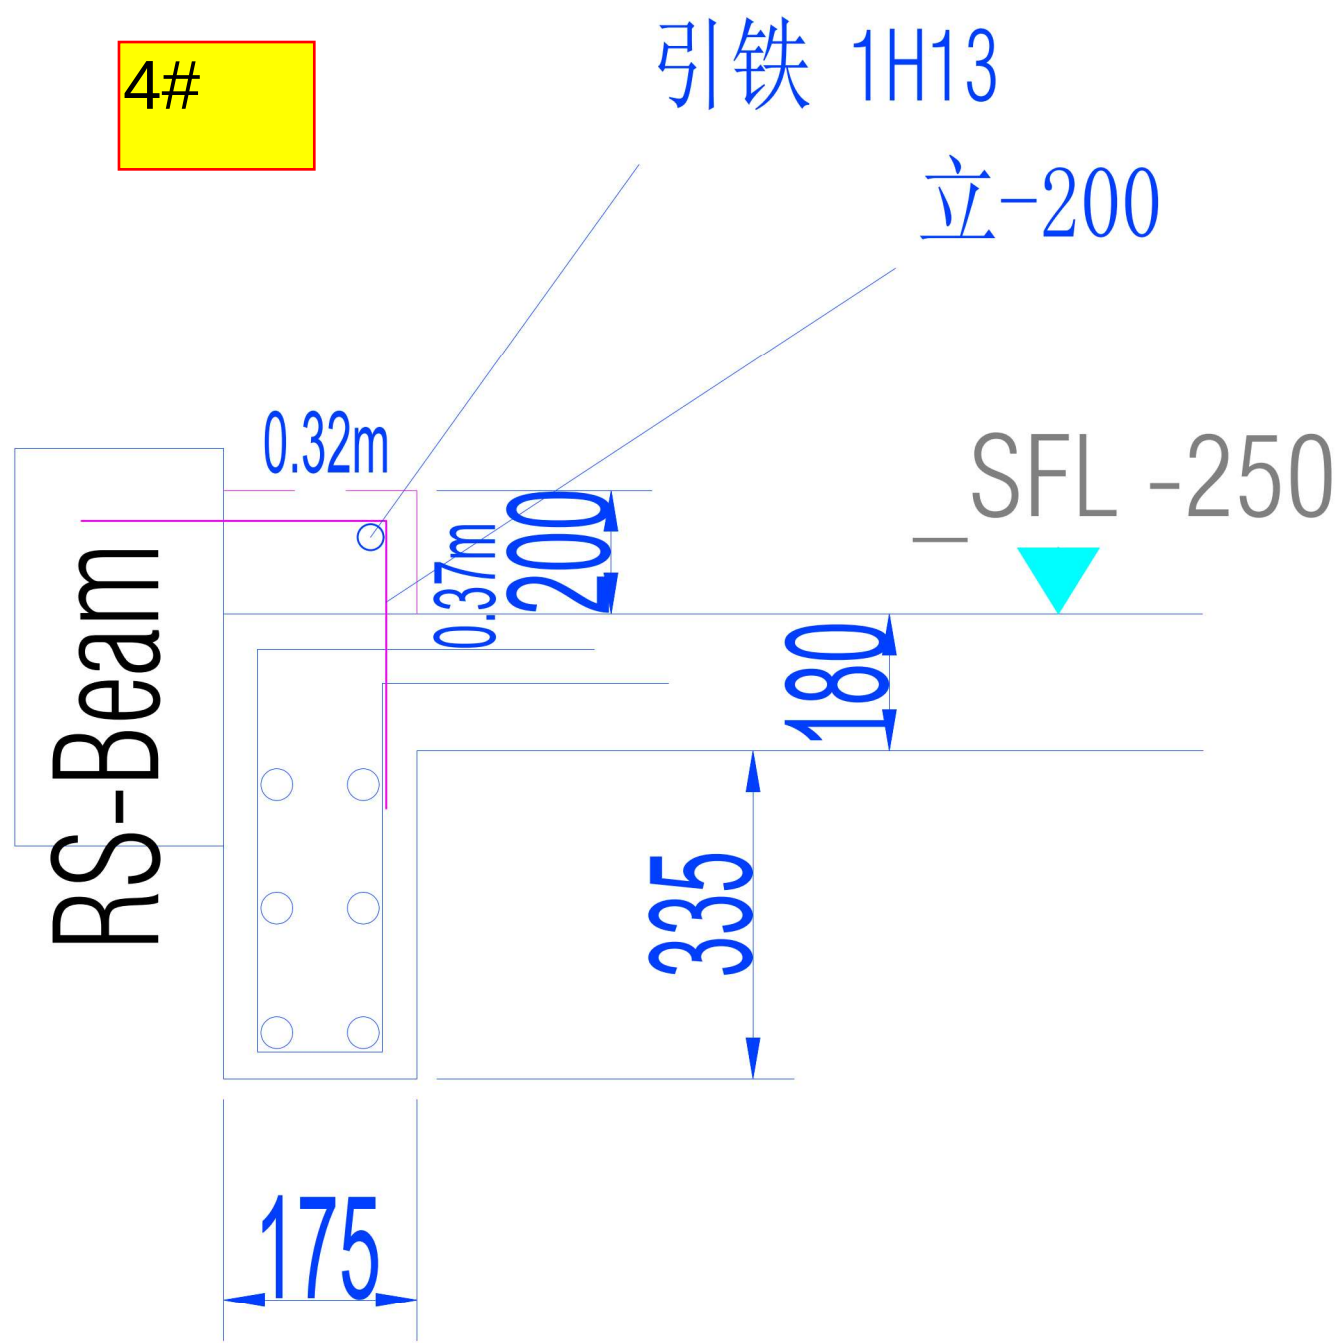



7#

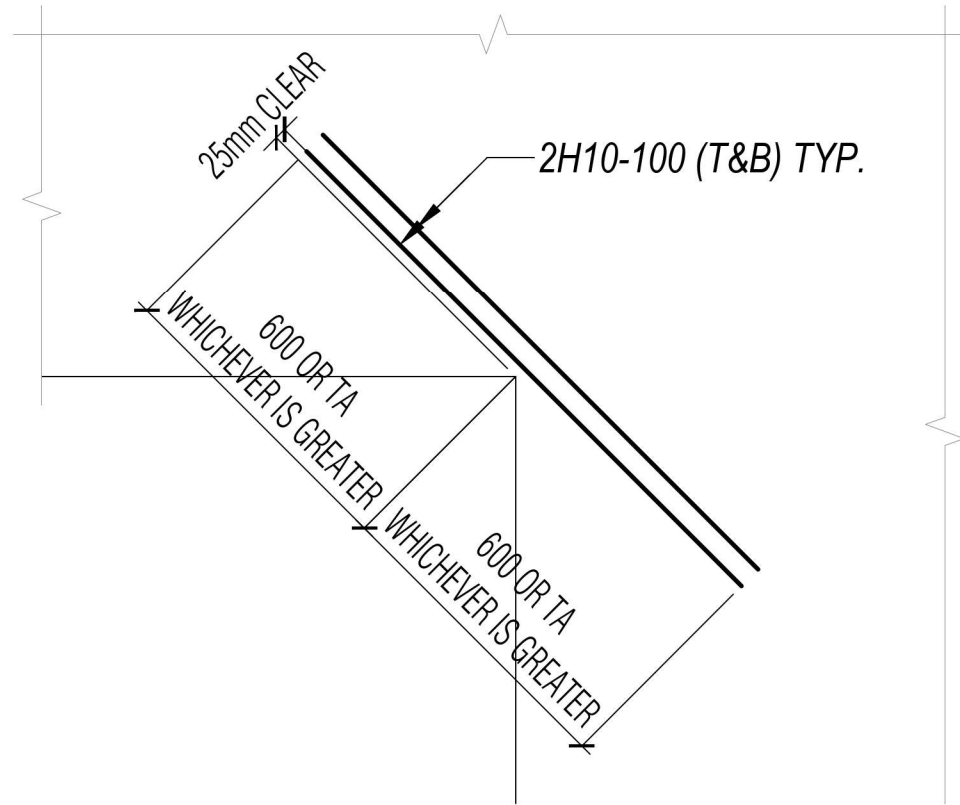

TYPICAL TRIMMER BARS AT RE-ENTRANT CORNER

SCALE : 1:25

